


# DRAFT HSA SUITE "D" PHASE II

ID	Task Mode	Task Name	Duration	Start	Qtr 1, 2021			Qtr 2, 2021		
					Jan	Feb	Mar	Apr	May	Jun
1										
2		<b>SUITE "D" INTERIOR REMODE</b>	<b>26 days</b>	<b>Mon 8/9/21</b>						
3		Bid Submission	1 day	Mon 8/9/21						
4		BOS Approval	0 days	Tue 8/24/21						
5		Notice of Award	0 days	Tue 8/31/21						
6		Notice to Proceed	0 days	Tue 9/14/21						
7		<b>CONSTRUCTION</b>	<b>153 days</b>	<b>Tue 9/21/21</b>						
8		Mobilization	5 days	Tue 9/21/21						
9		Demolition	32 days	Thu 9/30/21						
10		Interior Layout	10 days	Thu 11/18/21						
11		Modification MEP	35 days	Wed 11/24/21						
12		Interior Buildout	50 days	Mon 11/29/21						
13		Ceiling Grid Installation	20 days	Wed 2/2/22						
14		Remove & Replace Entry Do	5 days	Mon 1/31/22						
15		Painting	20 days	Mon 2/14/22						
16		Flooring & Base	15 days	Thu 3/17/22						
17		Closeout	7 days	Mon 4/11/22						
18		Demobilization	2 days	Wed 4/20/22						

INTERIOR REMODEL	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

# HSA SUITE "D" PHASE II

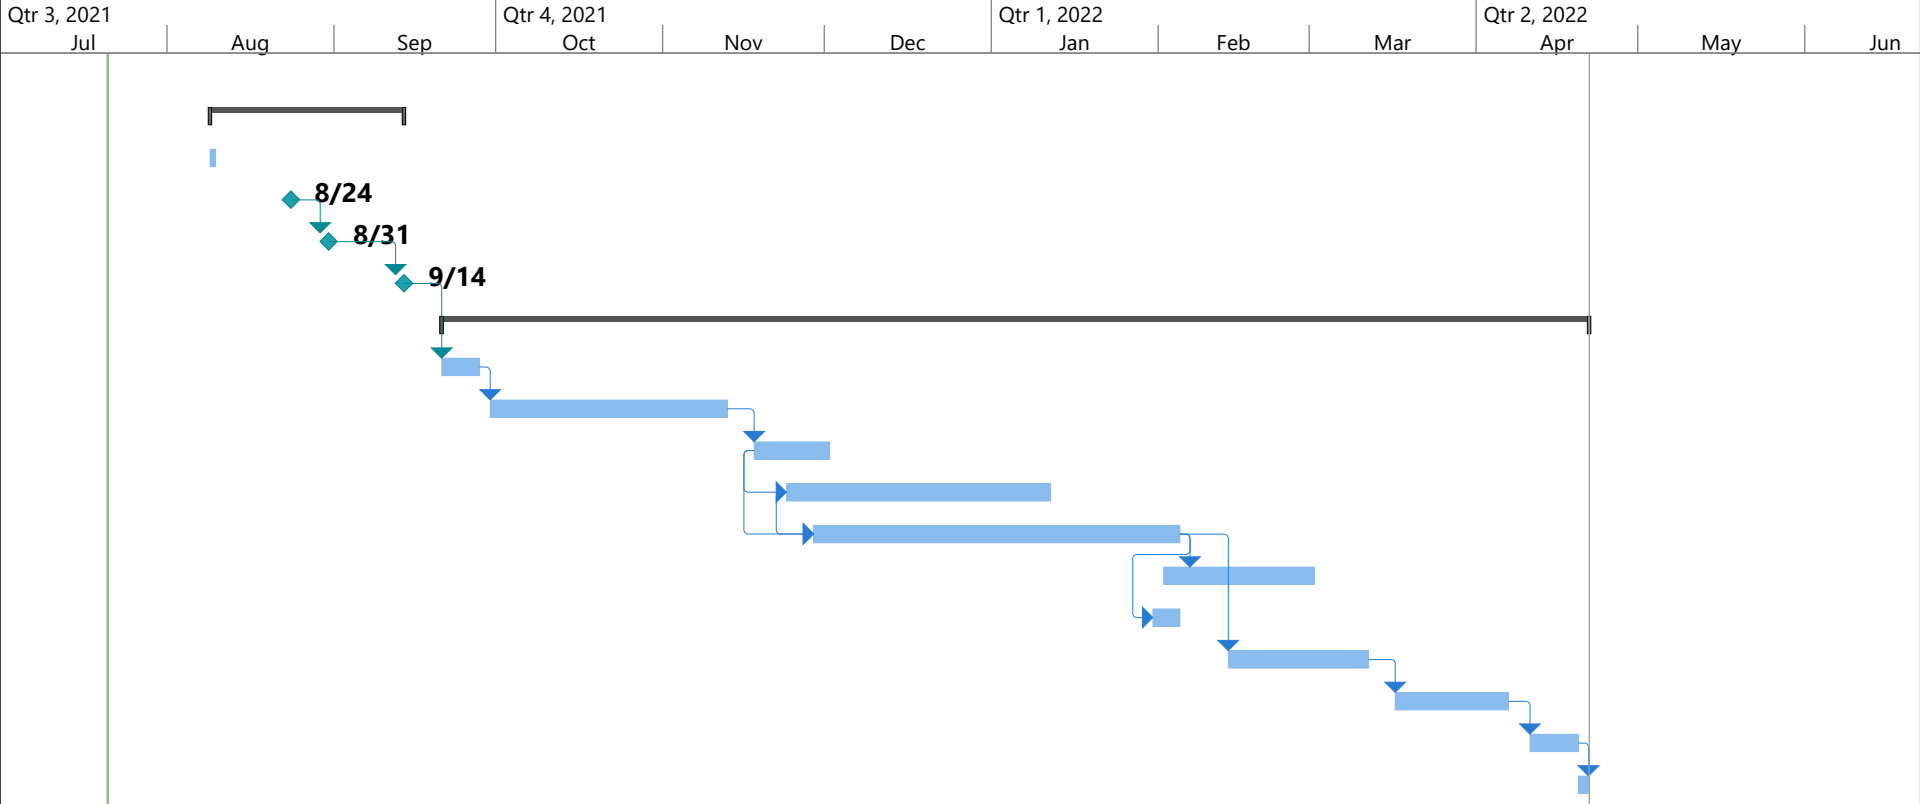

INTERIOR REMODEL	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
